


NEW MEXICO BROADBAND PROGRAM QUALITY ASSURANCE DASHBOARD August 2015

Project Overall Status: ● Scope ●
 Certification Phase: **Closeout** Budget ●
 Schedule ●


Project Objective: The National Broadband Program (NMBBP) now comes to a completion of five year funding cycle from the National Telecommunications and Information Administration (NTIA). This initiative was mapping the availability of broadband technologies and identifying methods to extend adoption into areas having inadequate services.

<http://www.doit.state.nm.us/broadband/isps.shtml>

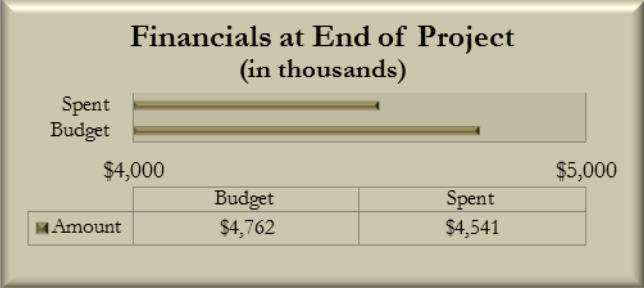

- ### Major Accomplishments
- NM Statewide Broadband Strategic Plan
 - NM Broadband Digital Literacy Strategic Plan
 - NM State Broadband Assessment: Education, Healthcare, and Economic Development
 - NM Statewide Parcel Data
 - Broadband Subscription and Internet Use in NM
 - NM Community Broadband Master Plan Guidebook
 - NM Regional Broadband Implementation Plan
 - Statewide Broadband Summit

- ### Lessons Learned
1. A clear scope, project plan, or technical standards had not been defined by NTIA
 2. A late start in adjusting the budget to acquire staff to assist in procurement and attend to the large amount of small details required by this project
 3. There were a number of budget details that made funds unavailable for a period of time towards the end of the project. This, with other factors resulted in the NMBBP having to return some funds back to NTIA
 4. In a project of this sort where one deliverable discovers the need for another contract deliverable, the amount of time to secure a contract needs to be scheduled clearly

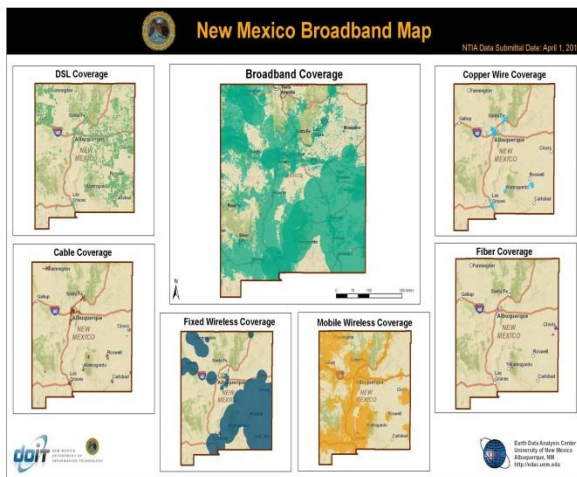

GOT BROADBAND?

DoIT's Interactive Web Map of Telecom Data, depicting:

- Broadband Availability
- Technology Types
- Providers offering these services
- Links to providers for more info

www.nmbbmapping.org



DoIT leadership has requested an agency Broadband Strategic Business Plan that will provide options to incorporate the programmatic functions of the grant requirements into the agency's business processes. Once that is completed in the beginning of Fall 2015, DoIT leadership will consider what options need additional funding and where that funding can be accessed.
